


ID	Task Mode	Task Name	Units	Duration	Start	Finish	Subcontractor	Predecessors	Quantity	Produ	Unit	October 2022
1		Construction		334 days	Tue 10/26/21	Fri 1/20/23						
89		Phase 5		131 days	Mon 6/27/22	Thu 12/22/22						
101		Blackhawk Trail (Lime)		9 days	Mon 12/12/22	Thu 12/22/22						
102		Pave 3" TY D HMAc	6,458.85 SY	2 days	Mon 12/12/22	Tue 12/13/22	ABR					
103		Pave Driveways	5.50 SY	2 days	Wed 12/21/22	Thu 12/22/22	ABR	102SS				
104		Bison Road (Lime)		1 day	Fri 12/9/22	Fri 12/9/22						
105		Pave 3" TY D HMAc	3,654.75 SY	1 day	Fri 12/9/22	Fri 12/9/22	ABR					
106		Hill Country Lane (Cement)		6 days	Wed 12/14/22	Wed 12/21/22						
107		Pave 3" TY D HMAc	13,088.56 SY	2 days	Wed 12/14/22	Thu 12/15/22	ABR					
108		Pave Driveways	150.48 SY	2 days	Tue 12/20/22	Wed 12/21/22	Asphalt Crew	107SS				
109		Phase 6		334 days	Tue 10/26/21	Fri 1/20/23						
110		Tomahawk Trail (Lime) (North Section)		40 days	Wed 11/23/22	Mon 1/16/23						
111		Street Excavation		4 days	Wed 12/14/22	Mon 12/19/22						
113		Mix-In 6" Lime Treated Subgrade	128.19 TNs	1 day	Thu 12/22/22	Thu 12/22/22	ABR		10582	2931 SY		
115		Remix Finish 6" Lime Subgrade	10,581.89 SY	2 days	Tue 12/27/22	Wed 12/28/22	ABR	114,123	10582	2931 SY		
116		Place 7" Flex Base	9,211.22 SY or 3,582 TNs	2 days	Thu 12/29/22	Fri 12/30/22	ABR	115	9211	1700 SY		
117		Pour Ribbon Curb	7,050.30 LF	7 days	Tue 1/3/23	Wed 1/11/23	Fox Quality Concrete					
118		Cure Ribbon Curb		1 day	Thu 1/12/23	Thu 1/12/23	Fox Quality Concrete	117				
119		Apply Prime Coat to Flex Base		1 day	Fri 1/13/23	Fri 1/13/23	ABR	118				
120		Pave 3" TY D HMAc	8,111.22 SY	2 days	Fri 1/13/23	Mon 1/16/23	ABR	119SS				
121		Pave Driveways	167.49 SY	2 days	Fri 1/13/23	Mon 1/16/23	ABR	120SS				
122		Winding Way (Long - Lime)		33 days	Wed 12/7/22	Fri 1/20/23						
123		Mix-In 6" Lime Treated Subgrade	124.30 TNs	2 days	Wed 12/7/22	Thu 12/8/22	ABR					
124		Cure Lime		2 days	Fri 12/9/22	Mon 12/12/22	ABR	123				
125		Remix Finish 6" Lime Subgrade	9,254.70 SY	1 day	Mon 12/12/22	Mon 12/12/22	ABR	124,115	9255	2931 SY		
126		Place 7" Flex Base	9,117.60 SY or 3,546 TNs	3 days	Tue 12/13/22	Thu 12/15/22	ABR	125	9118	1700 SY		
127		Finish Subgrade		4 days	Mon 12/19/22	Thu 12/22/22						
128		Pour Ribbon Curb	6,549 LF	6 days	Tue 1/3/23	Tue 1/10/23	Fox Quality Concrete	126				
129		Cure Ribbon Curb		1 day	Wed 1/11/23	Wed 1/11/23	Fox Quality Concrete	128				
130		Apply Prime Coat to Flex Base		1 day	Tue 1/17/23	Tue 1/17/23	ABR	121				
131		Pave 3" TY D HMAc	7,735.20 SY	4 days	Tue 1/17/23	Fri 1/20/23	ABR	130SS				
132		Pave Driveways	102.20 SY	1 day	Tue 1/17/23	Tue 1/17/23	ABR	131SS				
133		Crest Trail (Cement)		6 days	Thu 12/15/22	Thu 12/22/22						
134		Mix Existing 3" Asphalt	5,329.45 SY	1 day	Thu 11/10/22	Thu 11/10/22						
135		Cement Treat 7" Base	63.95 TNs	1 day	Tue 11/15/22	Tue 11/15/22	ABR		5329	4870 SY		
136		Cure Cement Treated 7" Base		1 day	Tue 11/15/22	Tue 11/15/22	ABR					
137		Pave 3" TY D HMAc	1,416.13 SY	1 day	Fri 12/16/22	Fri 12/16/22	ABR	145				
138		Cabin Path Street (Cement)		27 days	Fri 11/11/22	Fri 12/16/22						

Project: Project Schedule (Date: Tue 12/20/22


Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Mode	Task Name	Units	Duration	Start	Finish	Subcontractor	Predecessors	Quantity	Produ	Unit	October 2022
141		Cure Cement Treated 7" Base		1 day	Thu 11/17/22	Thu 11/17/22	ABR	140				
142		Pave 3" TY D HMA	1,416.13 SY	1 day	Fri 12/16/22	Fri 12/16/22	ABR	145				
143		Paso Del Norte Street (Cement)		310 days	Tue 10/26/21	Mon 12/19/22						
144		Cement Treat 7" Base	30.67 TNs or 2,556.25 SY	1 day	Wed 11/17/21	Wed 11/17/21	ABR		2556	4870 SY		
145		Cure Cement Treated 7" Base		1 day	Thu 11/18/21	Thu 11/18/21	ABR	144				
146		Pave 3" TY D HMA	1,416.13 SY	1 day	Mon 12/19/22	Mon 12/19/22	ABR	145				
150												
151												

Project: Project Schedule (Date: Tue 12/20/22)	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

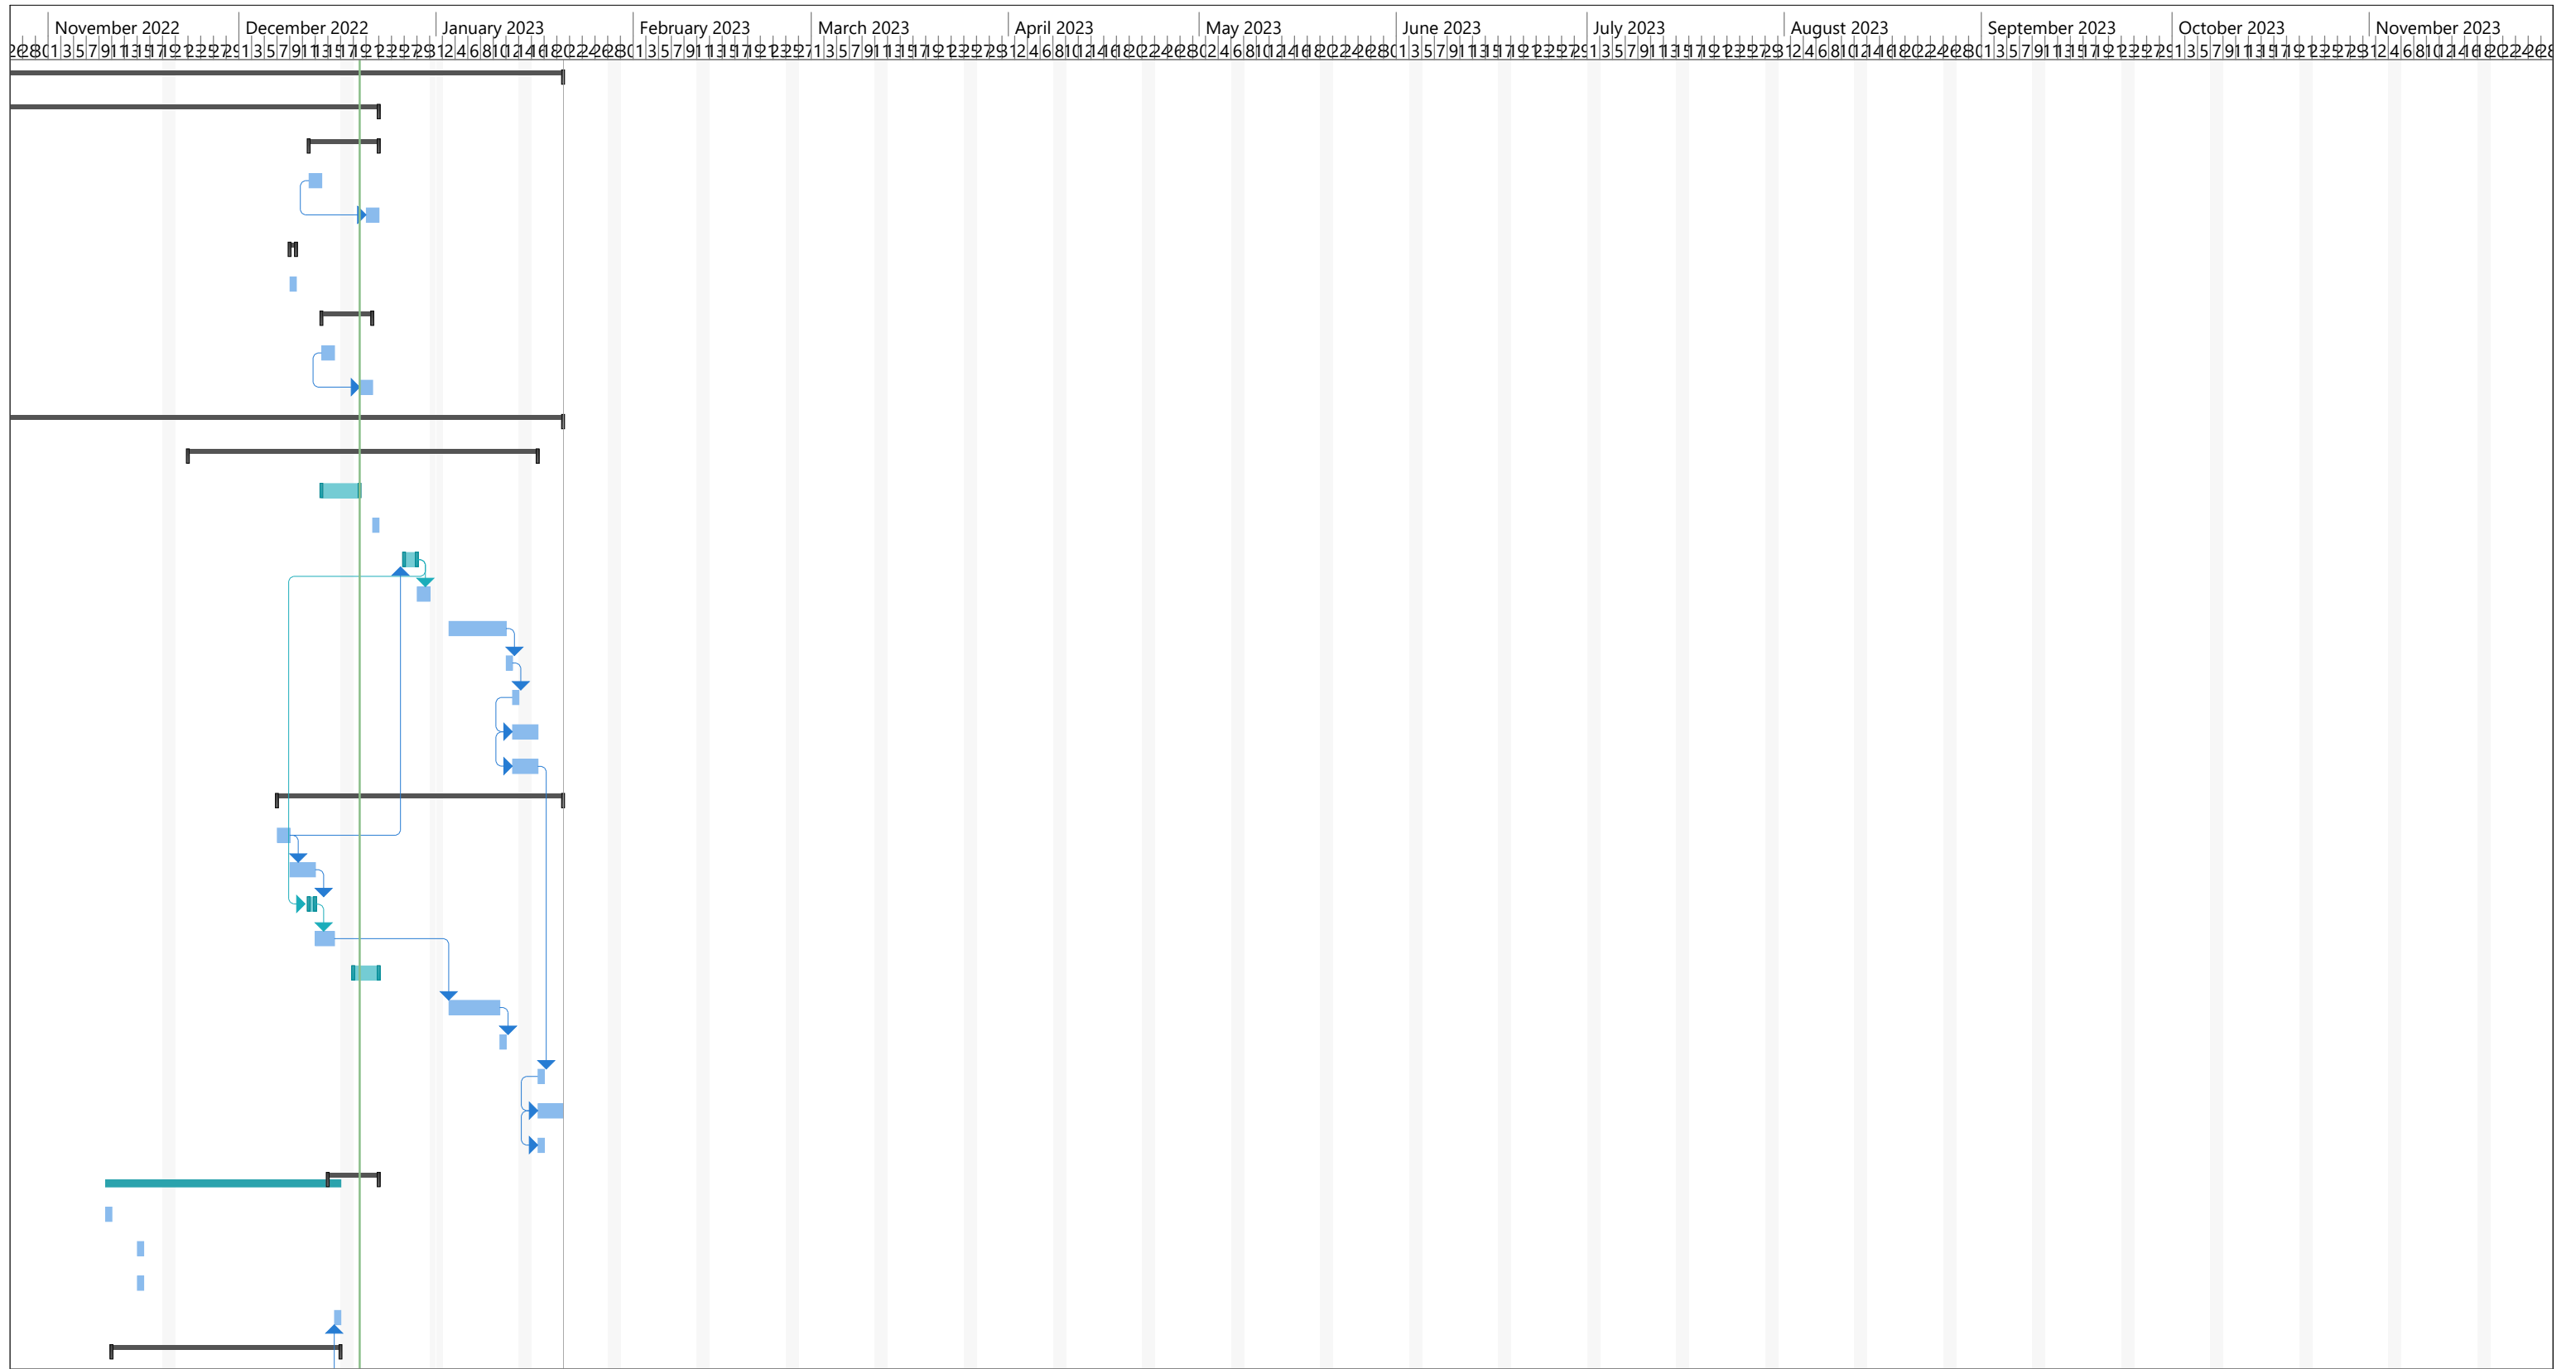

Project: Project Schedule (Date: Tue 12/20/22	Task	Project Summary	Manual Task	Start-only	Deadline
	Split	Inactive Task	Duration-only	Finish-only	Progress
	Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
	Summary	Inactive Summary	Manual Summary	External Milestone	

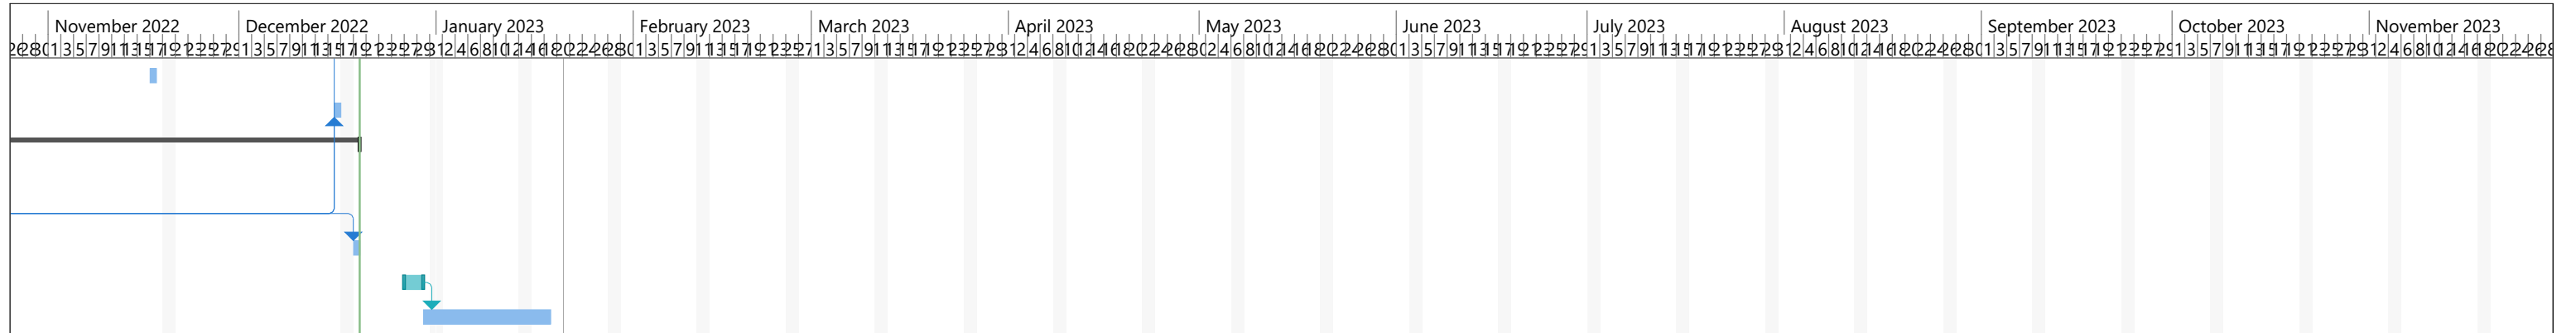

Project: Project Schedule (Date: Tue 12/20/22	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			
